



AFI Plan Aerodromes Certification Project Workshop for ESAF Region (Nairobi, Kenya, 23 - 26 August 2016)

Project Implementation Plan

*Arthemon Ndikumana
ICAO RO/AGA, Nairobi*




Outline

- AFI Plan Project Implementation phases
- Preliminary Schedule
- Preliminary Implementation dates
 - ✓ Preparedness review
 - ✓ Assistance in the certification
 - ✓ Monitoring/wrap up





Project phases

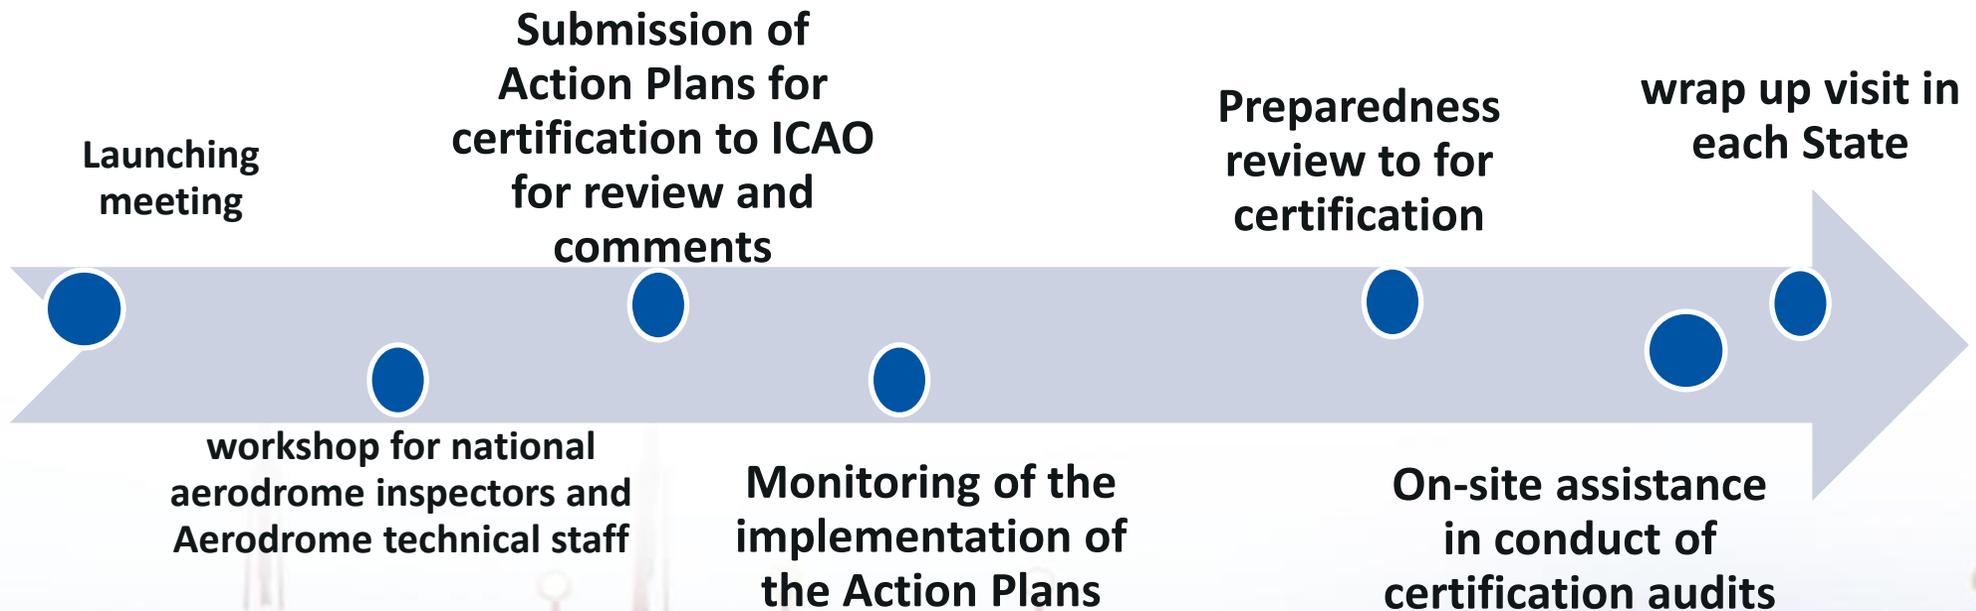




ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	08/08/16	01 Sep, '16	01 Nov, '16	01 Jan, '17	01 Mar, '17	01 May, '17	01 Jul, '17	01 Sep, '17
1	ESAF Aerodrome certification project	308 days	Mon 22/08/16	Wed 25/10/17										
2	Launching Meeting	1 day	Mon 22/08/16	Mon 22/08/16										
3	Workshop Nairobi	4 days	Tue 23/08/16	Fri 26/08/16	2	RO AGA,Resource								
4	Submission of action plans for certification to ICAO for review	21 days	Thu 15/09/16	Thu 13/10/16		States,RO AGA								
5	Monitoring of the implementation of action plans	88 days	Tue 01/11/16	Thu 02/03/17		RO AGA,Resource Expert								
6	Preparedness review	39 days	Mon 20/02/17	Thu 13/04/17										
15	Assistance in the certification	40 days	Mon 01/05/17	Fri 23/06/17										
24	Monitoring/wrap up	78 days	Mon 03/07/17	Wed 18/10/17										

Implementation Schedule


ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	01 Sep, '16	01 Nov, '16	01 Jan, '17	01 Mar, '17	01 May, '17	01 Jul, '17	01 Sep, '17
1	ESAF Aerodrome certification project	308 days	Mon 22/08/16	Wed 25/10/17									
2	Launching Meeting	1 day	Mon 22/08/16	Mon 22/08/16									
3	Workshop Nairobi	4 days	Tue 23/08/16	Fri 26/08/16	2	RO AGA,Resource							
4	Submission of action plans for certification to ICAO for review	21 days	Thu 15/09/16	Thu 13/10/16		States,RO AGA							
5	Monitoring of the implementation of action plans	88 days	Tue 01/11/16	Thu 02/03/17		RO AGA,Resource Expert							
6	Preparedness review	39 days	Mon 20/02/17	Thu 13/04/17									
7	Preparedness review 1	4 days	Mon 20/02/17	Thu 23/02/17									
8	Preparedness review 2	4 days	Mon 27/02/17	Thu 02/03/17									
9	Preparedness review 3	4 days	Mon 06/03/17	Thu 09/03/17									
10	Preparedness review 4	4 days	Mon 13/03/17	Thu 16/03/17									
11	Preparedness review 5	4 days	Mon 20/03/17	Thu 23/03/17									
12	Preparedness review 6	4 days	Mon 27/03/17	Thu 30/03/17									
13	Preparedness review 7	4 days	Mon 03/04/17	Thu 06/04/17									
14	Preparedness review 8	4 days	Mon 10/04/17	Thu 13/04/17									
15	Assistance in the certification	40 days	Mon 01/05/17	Fri 23/06/17									
24	Monitoring/wrap up	78 days	Mon 03/07/17	Wed 18/10/17									

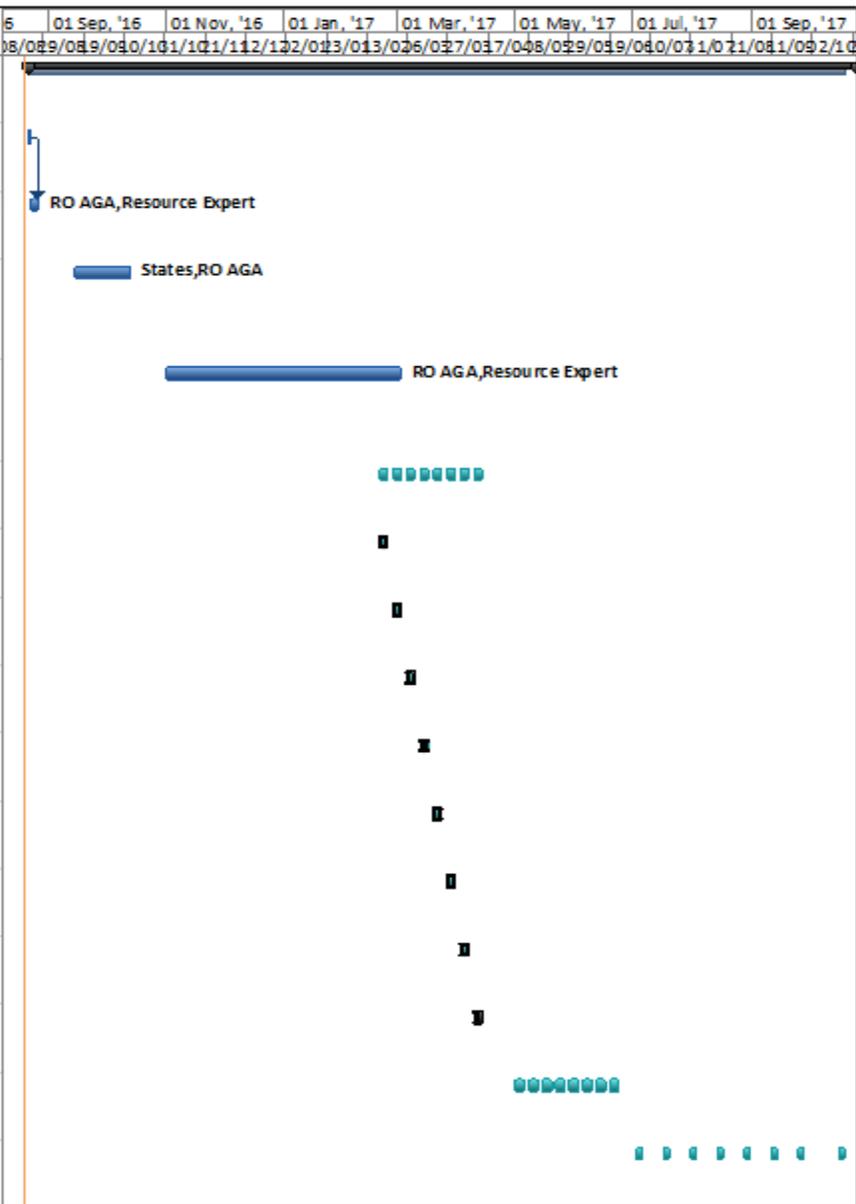

Preparedness Review



ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	08/08/16	01 Sep, '16	01 Nov, '16	01 Jan, '17	01 Mar, '17	01 May, '17	01 Jul, '17	01 Sep, '17
1	ESAF Aerodrome certification project	308 days	Mon 22/08/16	Wed 25/10/17										
2	Launching Meeting	1 day	Mon 22/08/16	Mon 22/08/16										
3	Workshop Nairobi	4 days	Tue 23/08/16	Fri 26/08/16	2	RO AGA,Resource								
4	Submission of action plans for certification to ICAO for review	21 days	Thu 15/09/16	Thu 13/10/16		States,RO AGA								
5	Monitoring of the implementation of action plans	88 days	Tue 01/11/16	Thu 02/03/17		RO AGA,Resource Expert								
6	Preparedness review	39 days	Mon 20/02/17	Thu 13/04/17										
15	Assistance in the certification	40 days	Mon 01/05/17	Fri 23/06/17										
16	Assistance in the certific	5 days	Mon 01/05/17	Fri 05/05/17										
17	Assistance in the certific	5 days	Mon 08/05/17	Fri 12/05/17										
18	Assistance in the certific	5 days	Mon 15/05/17	Fri 19/05/17										
19	Assistance in the certific	5 days	Mon 22/05/17	Fri 26/05/17										
20	Assistance in the certific	5 days	Mon 29/05/17	Fri 02/06/17										
21	Assistance in the certific	5 days	Mon 05/06/17	Fri 09/06/17										
22	Assistance in the certific	5 days	Mon 12/06/17	Fri 16/06/17										
23	Assistance in the certific	5 days	Mon 19/06/17	Fri 23/06/17										
24	Monitoring/wrap up	78 days	Mon 03/07/17	Wed 18/10/17										

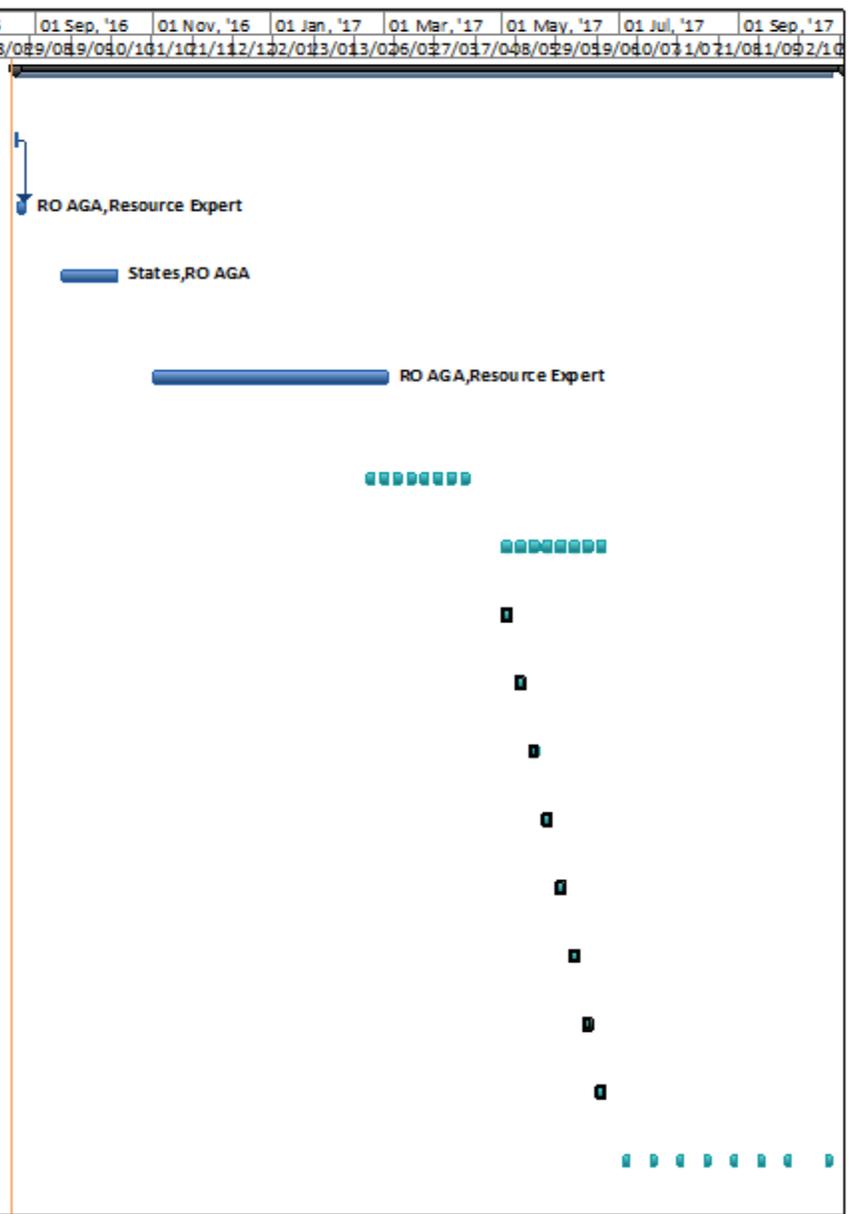

Assistance in the Certification

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	06/08/2016	01 Sep, '16	01 Nov, '16	01 Jan, '17	01 Mar, '17	01 May, '17	01 Jul, '17	01 Sep, '17
1	ESAF Aerodrome certification project	308 days	Mon 22/08/16	Wed 25/10/17										
2	Launching Meeting	1 day	Mon 22/08/16	Mon 22/08/16										
3	Workshop Nairobi	4 days	Tue 23/08/16	Fri 26/08/16	2	RO AGA,Resource								
4	Submission of action plans for certification to ICAO for review	21 days	Thu 15/09/16	Thu 13/10/16		States,RO AGA								
5	Monitoring of the implementation of action plans	88 days	Tue 01/11/16	Thu 02/03/17		RO AGA,Resource Expert								
6	Preparedness review	39 days	Mon 20/02/17	Thu 13/04/17										
15	Assistance in the certification	40 days	Mon 01/05/17	Fri 23/06/17										
24	Monitoring/wrap up	78 days	Mon 03/07/17	Wed 18/10/17										
25	Monitoring/wrap up 1	3 days	Mon 03/07/17	Wed 05/07/17										
26	Monitoring/wrap up 2	3 days	Mon 17/07/17	Wed 19/07/17										
27	Monitoring/wrap up 3	3 days	Mon 31/07/17	Wed 02/08/17										
28	Monitoring/wrap up 4	3 days	Mon 14/08/17	Wed 16/08/17										
29	Monitoring/wrap up 5	3 days	Mon 28/08/17	Wed 30/08/17										
30	Monitoring/wrap up 6	3 days	Mon 11/09/17	Wed 13/09/17										
31	Monitoring/wrap up 7	3 days	Mon 25/09/17	Wed 27/09/17										
32	Monitoring/wrap up 8	3 days	Mon 16/10/17	Wed 18/10/17										

Monitoring/Wrap Up



Travel Arrangements		
From	To	Back
Preparedness Review		
Nairobi	Luanda	Nairobi
Johannesbourg	Maputo	Johannesbourg
Johannesbourg	Windhoek	Johannesbourg
Nairobi	Kigali	Nairobi
Addis	Seychelles	Addis
Addis	Entebbe	Addis
Nairobi	Lusaka	Nairobi
Abidjan	Antananarivo	Abidjan
Assistance for Certification		
Johannesbourg	Luanda	Johannesbourg
Addis	Maputo	Addis
Nairobi	Windhoek	Nairobi
Johannesbourg	Kigali	Johannesbourg
Nairobi	Seychelles	Nairobi
Nairobi	Entebbe	Nairobi
Addis	Lusaka	Addis
Abidjan	Antananarivo	Abidjan
Monitoring/Wrap up		
Nairobi	Luanda	Nairobi
Nairobi	Maputo	Nairobi
Nairobi	Windhoek	Nairobi
Nairobi	Kigali	Nairobi
Nairobi	Seychelles	Nairobi
Nairobi	Entebbe	Nairobi
Nairobi	Lusaka	Nairobi
Nairobi	Antananarivo	Nairobi



ICAO

North American
Central American
and Caribbean
(NACC) Office
Mexico City

South American
(SAM) Office
Lima

ICAO
Headquarters
Montréal

Western and
Central African
(WACAF) Office
Dakar

European and
North Atlantic
(EUR/NAT) Office
Paris

Middle East
(MID) Office
Cairo

Eastern and
Southern African
(ESAF) Office
Nairobi

Asia and Pacific
(APAC) Sub-office
Beijing

Asia and Pacific
(APAC) Office
Bangkok



THANK YOU
