IIM COM 5 PROJECT PLANNING – MAY 2023 (1/2)

2023

IIM/SG-COM PROJECT N°5 PLANNING

« ASSESSMENT OF AFI AIR NAVIGATION SERVICES CYBER RESILIENCE »

Schedule

		Lead	Start	Durati		Due	Recalculate start	Recalculate end	Progre
1.4	Develop Project Questionnaire	Sandrine	01/02/18	60	d	16/09/18	01/02/18	16/09/18	100%
1.5	Update List of project members	Secretari	15/15/2020	5	d	31/03/21	15/15/2020	31/03/21	100%
1.6	Develop Project Cost estimation	Sandrine	30/01/23	120	d	30/05/23	30/01/23	30/05/23	20%
1.7	Develop Project Organization description	SANDRINE	15/03/18	2	d	31/10/18	15/03/18	31/10/18	100%
1.8	Develop Project planning (initial)	SANDRINE	01/10/18	2	d	30/11/18	01/10/18	30/11/18	100%
1.9	Development of Terms of reference (2018)	SANDRINE	01/09/18	2	d	01/11/18	01/09/18	01/11/18	100%
1.10	Develop Project meeting schedule (update)	SANDRINE	30/01/23	5	d	04/02/23	30/01/23	04/02/23	100%
MS	Progress meeting n° 1		15/01/201						
1.11	Update of project documentation (alignement with 6th edition of GANP)	SANDRINE	30/10/22	25	d	24/11/22	30/10/22	24/11/22	100%
	Progress meeting n° 2		28/06/21						100%
2	**Assessment of the current AFI ANS Cyber resilience**		25/03/19	1527		29/05/23	25/03/19	29/05/23	100%
2.1	Develop the project questionnaire to AFI States and AN	ALL	20/11/20		d	20/02/21	20/02/21	20/11/20	100%
2.2	Send the project questionnaire to AFI States and ANSF	SANDRINE	20/11/20		d	20/02/21	20/02/21	20/11/20	100%
2.3	Analyze AFI States data gathered through the project q	FREDRICK	30/09/22	60	d	29/11/22	30/09/22	29/11/22	100%
2.4	Develop a survey report 2022		25/11/22	30	d	25/12/22	25/11/22	25/12/22	100%
2.5	Analyze AFI States data gathered through the project q	FREDRICK	30/03/23	30	d	29/04/23	30/03/23	29/04/23	100%
2.6	Develop a survey report 2023		29/04/23	30	d	29/05/23	29/04/23	29/05/23	100%
2.7	**Final feedback questionnaire analysis**		30/05/23						100%
2.8	Progress meeting		02/03/203						100%
2.9	Identify cyber threats to ANS in AFI Region		25/03/19	60	d	31/09/2019	25/03/19	31/09/2019	100%
2.10	Progress meeting		30/06/22						100%
2.11	Progress meeting		30/07/23						100%
MS	**Milestone [D04] (current state of AFI ANS Cyber safety**		30/06/23						100%
3	**AFI Global cyber resilience framework**		15/01/19	1657		29/07/23	15/01/19		100%
3.1	Develop scope and structure of the framework	FREDRICK	15/01/19	25	d	08/02/19	15/01/19	08/02/19	100%
3.2	Develop all the chapters of the framework	FREDRICK	08/02/19	270	d	04/11/19	08/02/19	04/11/19	100%
3.3	Participate in Working session with cyber security in av	ALL	04/12/19	4	d	07/12/19	04/12/19	07/12/19	100%
3.4	Project Progress meeting	SANDRINE	15/10/19			15/10/19			100%
3.5	Develop Revised Edition of AFI ANS cyber resilience fra		15/12/20	90	d	14/03/21	15/12/20	14/03/21	100%
2.10	Progress meeting		30/06/21						100%
3.7	Progress meeting	SANDRINE	30/11/21			30/06/21			100%
3.8	Progress meeting		28/05/22			28/09/21			100%
3.9	Participation in cyber security in aviation seminar	Sandrine	30/12/22	40	d	07/02/23	30/12/22	07/02/23	100%
4.5	Revised Edition of AFI ANS cyber resilience framework	Sandrine	20/04/22	60	d	18/06/22	20/04/22	18/06/22	100%
3.10	Revised Edition of AFI ANS cyber resilience framework	Sandrine	20/02/23	100	d	30/05/23	20/02/23	30/05/23	100%

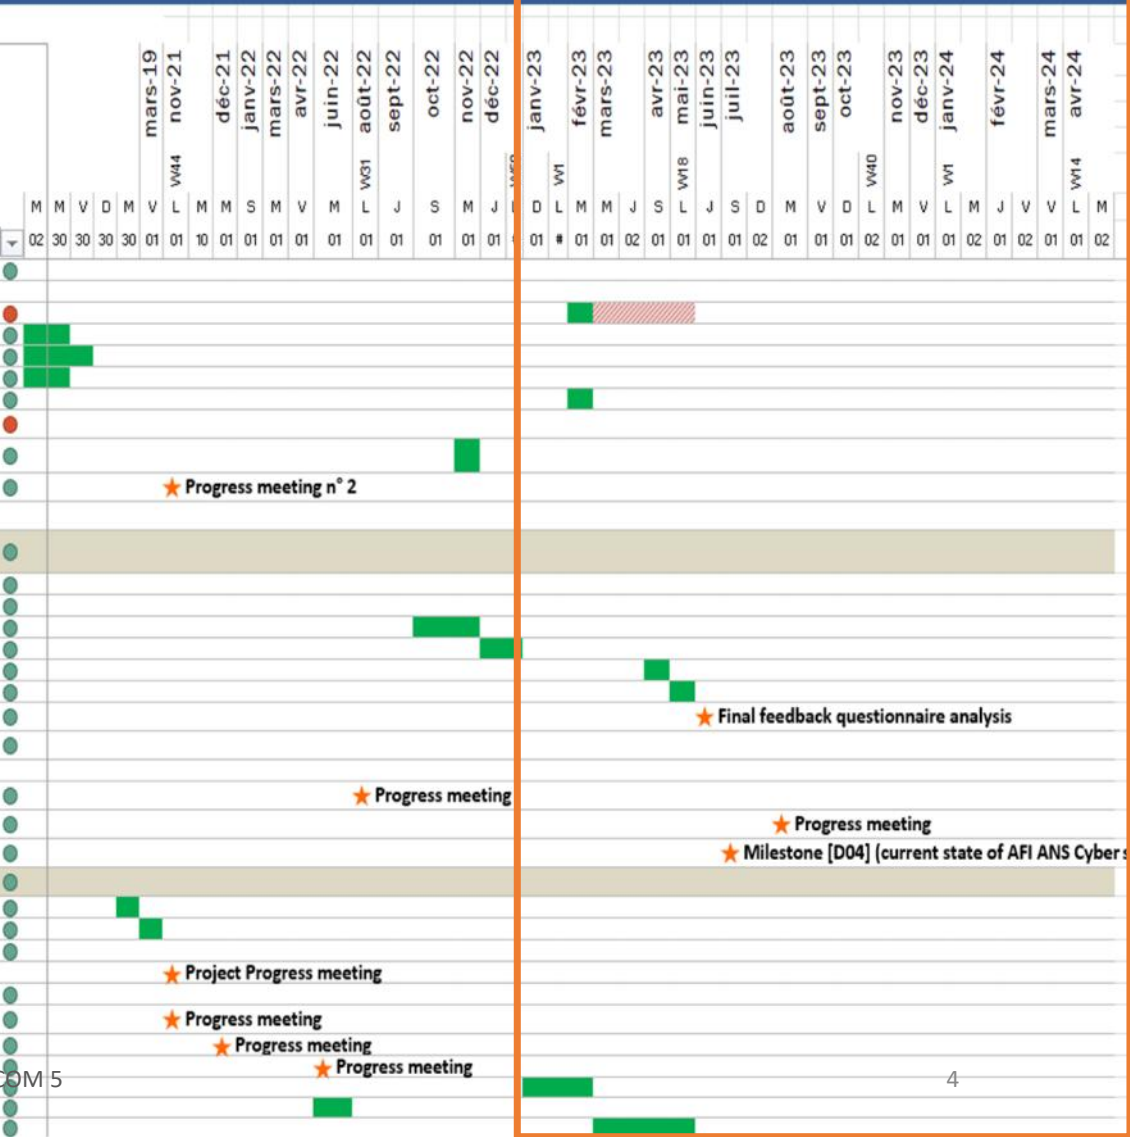

2023

IIM/SG-COM Project N°5 Planning

« Assessment of AFI Air Navigation Services Cyber Resilience »

Schedule
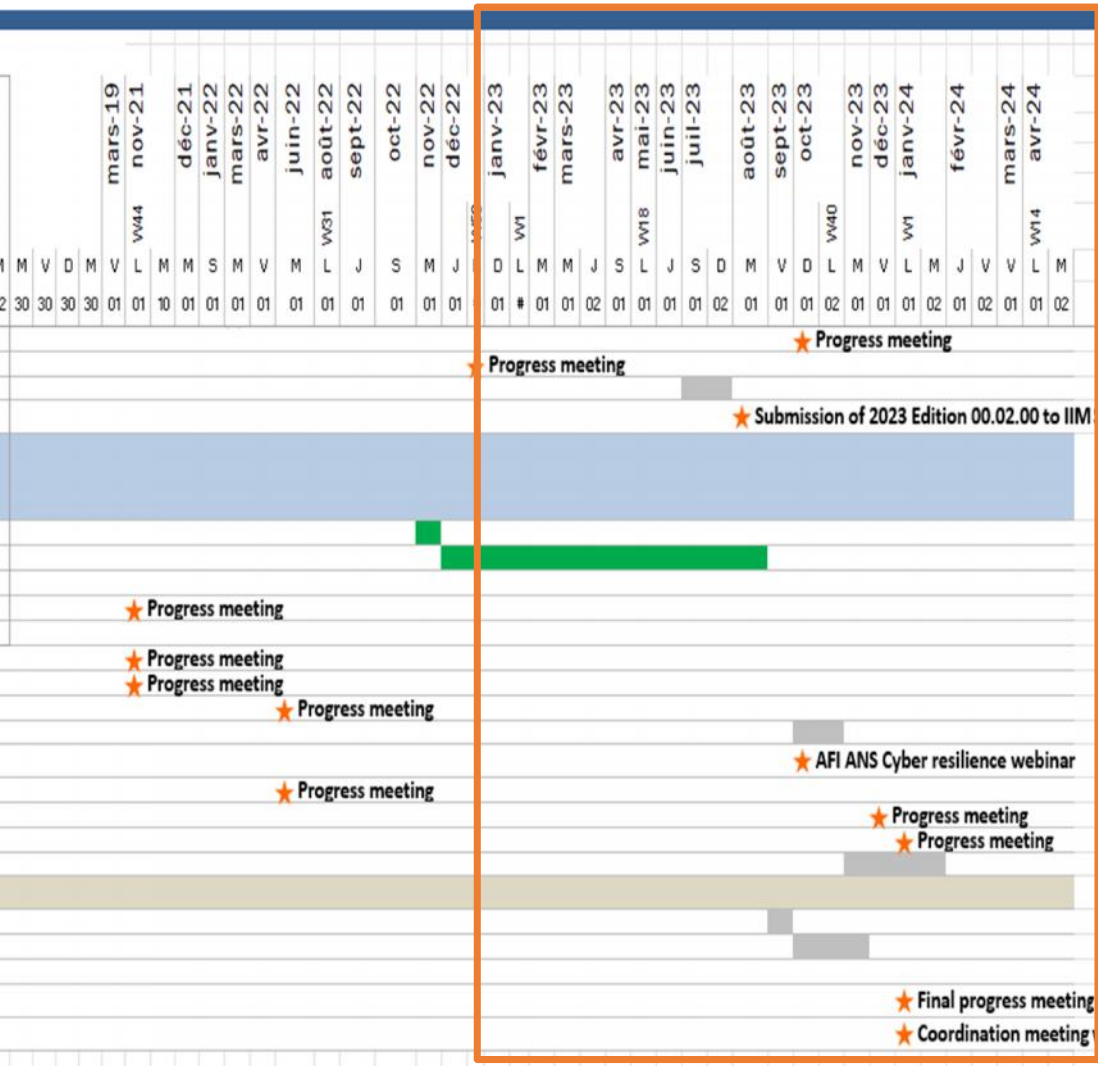
		Lead	Start	Durati		Due	Recalculated start	Recalculated end	Progre
3.12	Progress meeting		28/09/23			28/05/22			
3.13	Progress meeting		13/12/22			28/11/22			
3.10	Review of Edition of AFI ANS cyber resilience framewor	Sandrine	30/06/23	30	d	29/07/23	30/06/23	29/07/23	0%
MS	Submission of 2023 Edition 00.02.00 to IIM SG Secret		30/07/23	1	d	30/07/21			
4	AFI Air Navigation Services Cyber resilience awareness	FREDRI(	04/12/19	1342		06/08/23			100%
4.1	Identify an review available aviation training courses	Sandrine	01/11/22	10	d	10/11/22	01/11/22	10/11/22	100%
4.2	planning of at least two workshops on cybersecurity of	FREDRICK	10/11/22	270	d	06/08/23	10/11/22	06/08/23	100%
4.2	Working session with cyber security in aviation experts	Secretari	04/12/19	4	d	07/12/19	04/12/19	07/12/19	100%
	Progress meeting	SANDRINE	15/10/19			15/10/19			100%
4.3	Revised Edition of AFI ANS cyber resilience framework		15/11/20	60	d	13/01/21	15/11/20	13/01/21	100%
	Progress meeting	SANDRINE	28/11/20			28/11/20			100%
	Progress meeting	SANDRINE	30/03/21			30/01/21			
	Progress meeting		28/05/22			28/03/21			
4.4	Working session with cyber security in aviation experts	Sandrine	30/09/23	4	d	03/10/23	30/09/23	03/10/23	0%
MS	AFI ANS Cyber resilience webinar		30/09/23	1	d	30/09/23			
	Progress meeting		28/04/22			28/04/22			
	Progress meeting		28/11/23			28/05/22			
	Progress meeting		28/12/23			28/06/22			
4.6	Workshop on ANS AFI Cyber safety and resilience	Sandrine	04/10/23	120	d	31/01/24	04/10/23	31/01/24	0%
5	AFI ANS Cyber resilience communication	Sandrin	30/08/23	84		21/11/23			3%
4.1	Develop a project plan communication	Sandrine	30/08/23	25	d	23/09/23	30/08/23	23/09/23	0%
4.2	Develop short key messages	Sandrine	23/09/23	60	d	21/11/23	23/09/23	21/11/23	10%
4.2	Working session with other IIM projects	Sandrine	30/10/23	2	d	31/10/23	30/10/23	31/10/23	0%
MS	Final progress meeting (close out meeting)		20/12/23	1	d				
	Coordination meeting with IIM Secretariat		15/12/23	1	d
